ROBSON CIVIL PROJECTS

6228 SCC Upgrade

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
0		6228 SCC Upgrade	331 days?	Mon 1/07/1	Wed 18/11	
1		Project Milestones	262 days	Mon 1/07/1	Fri 7/08/20	
10		Approvals	43 days	Tue 16/06/2	Thu 13/08/2	
15		Procurement	253 days	Mon 1/07/1	Mon 27/07/	
26		Construction	331 days?	Mon 1/07/1	Wed 18/11/	
27		**Mobilisation and Management Plans**	**45 days**	**Tue 16/06/20**	**Mon 17/08/2**	
32		**Establishment**	**29 days**	**Mon 3/08/20**	**Thu 10/09/20**	
33		Tree Removal	15 days	Mon 3/08/20	Fri 21/08/20	
34		Erosion & sediment control	5 days	Mon 3/08/20	Fri 7/08/20	30FF
35		Ausgrid Approval to proceed	0 days	Mon 17/08/2	Mon 17/08/2	
36		Clear & mulch trees - 9 ea	5 days	Mon 17/08/2	Fri 21/08/20	35
37		Remove mulch from site	2 days	Thu 20/08/20	Fri 21/08/20	36FF
38		Traffic and Pedestrian Management	3 days	Mon 3/08/20	Wed 5/08/20	
39		Set Up Long Term Speed Reduction Signage	3 days	Mon 3/08/20	Wed 5/08/20	30SS
40		Demolition	5 days	Mon 10/08/2	Fri 14/08/20	
41		Remove Median Island John Street (Day)	2 days	Mon 10/08/2	Tue 11/08/20	30,39
42		Remove Roundabout Splinter Island - John St	3 days	Wed 12/08/2	Fri 14/08/20	41
43		Drainage	12 days	Wed 26/08/2	Thu 10/09/20	
44		Remediation of Stormwater Drainage Line	7 days	Wed 26/08/2	Thu 3/09/20	39FS+14 days
46		**Block 4**	**310 days**	**Mon 1/07/19**	**Mon 19/10/2**	
47		Block 4 Phase 1	15 days	Thu 6/08/20	Wed 26/08/2	
48		Set Up Pedestrian Management	2 days	Thu 6/08/20	Fri 7/08/20	39
49		Remove Existing Pavers and Bricks	6 days	Mon 10/08/2	Mon 17/08/2	48
50		Remove Street Signs	2 days	Thu 6/08/20	Fri 7/08/20	48SS
51		Service search	1 day	Tue 18/08/20	Tue 18/08/20	49
52		Saw Cut Electrical Trench	1 day	Wed 19/08/2	Wed 19/08/2	51
53		Excavate/Install services/Backfill including property connections	5 days	Thu 20/08/20	Wed 26/08/20	52
54		Pour concrete slab	5 days	Thu 20/08/20	Wed 26/08/2	53FF
55		Block 4 Phase 2	35 days	Thu 27/08/20	Mon 19/10/2	
56		Set up traffic control (Iron men in parking lane / pedestrian fence on footpath)	1 day	Thu 27/08/20	Thu 27/08/20	54
57		Sawcut against kerb	1 day	Fri 28/08/20	Fri 28/08/20	56
58		Remove existing kerb	3 days	Mon 31/08/2	Wed 2/09/20	57
76		**Block 9**	**267 days?**	**Mon 1/07/19**	**Fri 14/08/20**	
77		Block 9 Phase 1	267 days?	Mon 1/07/19	Fri 14/08/20	
78		Set up pedestrian management	1 day	Mon 10/08/2	Mon 10/08/2	30
79		Kiosk Preperation Works	5 days	Mon 10/08/2	Fri 14/08/20	78SS
80		Excavate and install electrical along park	5 days	Mon 10/08/2	Fri 14/08/20	79SS
96		**Block 8**	**294 days**	**Mon 1/07/19**	**Wed 23/09/2**	
97		Block 8 Crossing	2 days	Mon 17/08/2	Tue 18/08/20	
98		Set up traffic control northern half (contra flow	1 day	Mon 17/08/2	Mon 17/08/2	80
99		Saw cut road	1 day	Mon 17/08/2	Mon 17/08/2	98SS
100		Excavate northern end of trench	1 day	Mon 17/08/2	Mon 17/08/2	98SS
101		Install conduits / backfill to finish level	1 day	Mon 17/08/2	Mon 17/08/2	98SS
102		Set up traffic control southern half (contra flow	1 day	Tue 18/08/20	Tue 18/08/20	101
103		Saw cut road / demolish kerb	1 day	Tue 18/08/20	Tue 18/08/20	102SS
104		Excavate southern end of trench	1 day	Tue 18/08/20	Tue 18/08/20	102SS
105		Install conduits / backfill to finish level	1 day	Tue 18/08/20	Tue 18/08/20	102SS
106		Block 8 Phase 1	17 days	Tue 11/08/20	Wed 2/09/20	
107		Set Up Pedestrian Management	1 day	Tue 11/08/20	Tue 11/08/20	78
108		Remove existing pavers and bricks	2 days	Wed 12/08/2	Thu 13/08/20	107
109		Remove existing street signs	1 day	Wed 12/08/2	Wed 12/08/2	108SS
110		Service search	1 day	Fri 14/08/20	Fri 14/08/20	108
111		Saw Cut Electrical Trench	1 day	Wed 19/08/2	Wed 19/08/2	110FS+2 days
112		Excavate/Install services/backfill (including property connections)	10 days	Thu 20/08/20	Wed 2/09/20	111
114		Block 8 Phase 2	294 days	Mon 1/07/19	Wed 23/09/2	
115		Set up traffic control (stop and go)	1 day	Wed 19/08/2	Wed 19/08/2	105
116		Saw cut against kerb	1 day	Wed 19/08/2	Wed 19/08/2	115SS
117		Set up traffic control (iron men reducing travel lane to 3.2m)	1 day	Thu 20/08/20	Thu 20/08/20	116
118		Remove existing kerb	5 days	Fri 21/08/20	Thu 27/08/20	117
119		Install lightpole footings	3 days	Fri 28/08/20	Tue 1/09/20	118
135		**Block 3**	**331 days?**	**Mon 1/07/19**	**Wed 18/11/2**	
136		Block 3 Phase 1	15 days	Tue 18/08/20	Mon 7/09/20	
137		Set Up Pedestrian Management	1 day	Tue 18/08/20	Tue 18/08/20	49
138		Remove Existing Pavers and Bricks	6 days	Tue 18/08/20	Tue 25/08/20	137SS
139		Remove Street Signs	2 days	Mon 24/08/2	Tue 25/08/20	138FF
140		Service search	1 day	Wed 26/08/2	Wed 26/08/2	139
141		Saw Cut Electrical Trench	1 day	Mon 31/08/2	Mon 31/08/2	140FS+2 days
164		**Block 6**	**296 days?**	**Mon 1/07/19**	**Fri 25/09/20**	
165		Block 6 Phase 1	21 days	Thu 27/08/20	Fri 25/09/20	
166		Set Up Pedestrian Management	1 day	Thu 27/08/20	Thu 27/08/20	54
167		Remove Existing Pavers and Bricks	6 days	Fri 28/08/20	Fri 4/09/20	166

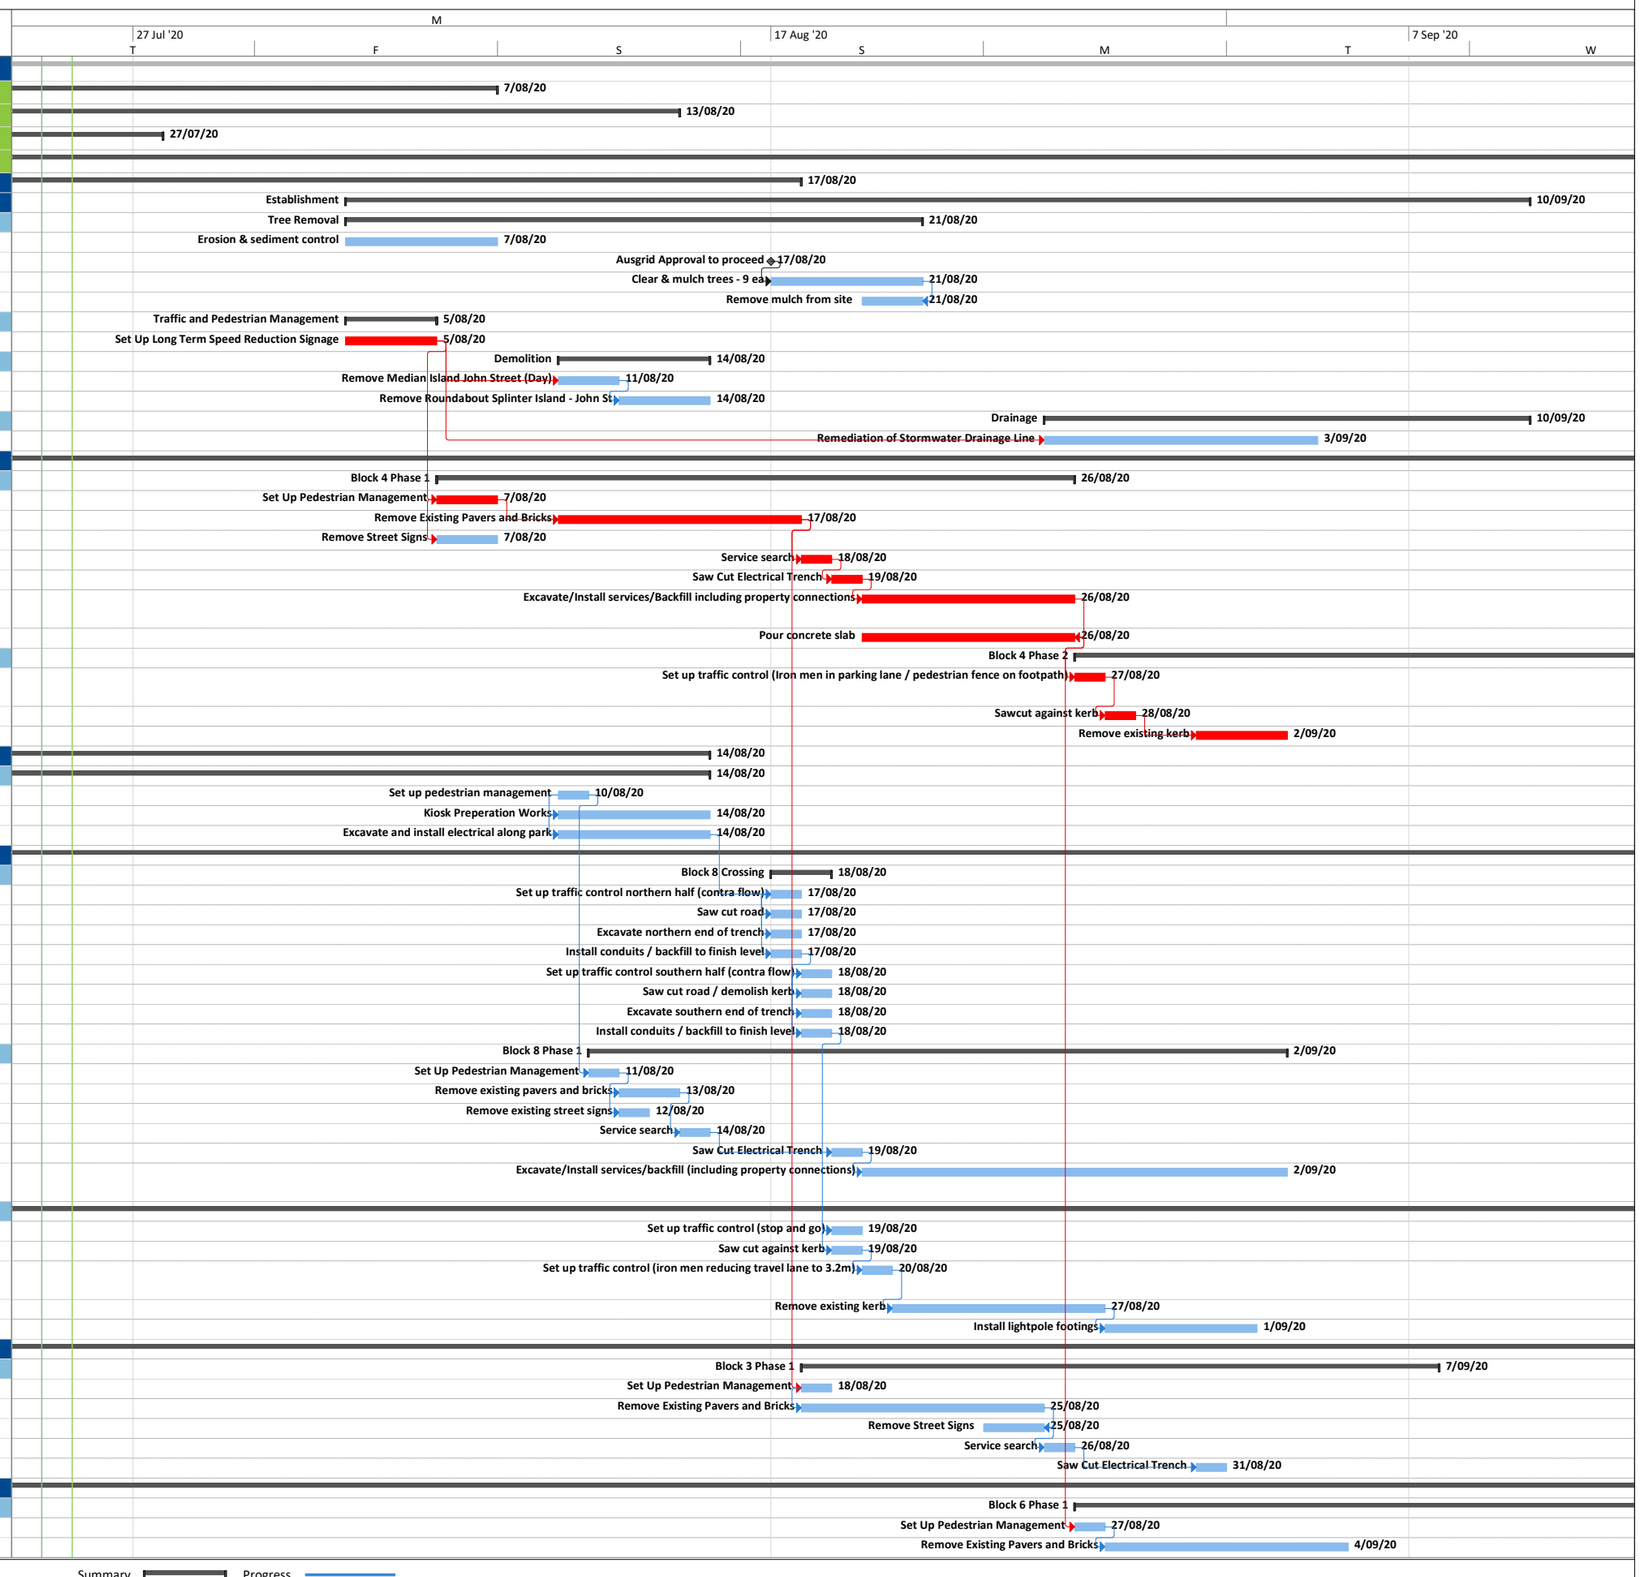

Project: 6228 SCC Upgrade
Date: Fri 24/07/20
Page 1 of 1

Task | Critical | Milestone | Summary | Progress
